

NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION

(1) County Putnam



(3) DEC Well Number P1564

(2) Township Mahopac

WELL COMPLETION REPORT

LOG *

Ground Surface EL. _____ ft. above sea level

(4) OWNER
Jim Battista

(5) ADDRESS
C/O Vito Torchia, 33 Cook Drive, Mahopac, NY 10541

(6) LOCATION OF WELL (See Instructions On Reverse)
Show Lat/Long if available and method used:
Cook Drive, Mahopac, NY
 GPS DEC Website Map Interpolation

Top Of Casing is located +1 ft. above (+) or below (-) ground surface

(7) DEPTH OF WELL BELOW LAND SURFACE (Feet) **665'** **5 1/2 gpm**

(8) DEPTH TO GROUNDWATER BELOW LAND SURFACE (Feet) **N/A** DATE MEASURED _____

TOP OF WELL

CASINGS

(8) DIAMETER
6" in. | | | | in.

0'
Drilling in overburden clay and boulders

(10) LENGTH
42' ft. | | | | in.

(11) GROUT TYPE / SEALING **portland cement**

(12) GROUT / SEALING INTERVAL (Feet) FROM **5'** TO **42'**

SCREENS

(13) MAKE & MATERIAL _____ (14) OPENINGS _____

5'
Drilling in rock for casing

(15) DIAMETER _____ in. | | | | in.

(16) LENGTH _____ ft. | | | | in.

(17) DEPTH TO TOP OF SCREEN, FROM TOP OF CASING (Foot) _____

YIELD TEST

(18) DATE **2/27/01** (19) DURATION OF TEST **6 hours**

42'
Set 42' of 6" casing

(20) LIFT METHOD Pump Air Lift Bail (21) STABILIZED DISCHARGE (GPM) **5 gpm**

Drilling in rock granite

(22) STATIC LEVEL PRIOR TO TEST (feet/inches below top of casing) **30'** (23) MAXIMUM DRAWDOWN (Stabilized) (feet/inches below top of casing) **600'**

(24) RECOVERY (Time in hours/minutes) **2 hours** (25) Was the water produced during test discharged away from immediate area? Yes No _____

PUMP INSTALLATION

(26) PUMP INSTALLED? YES NO _____ (27) DATE **2/27/01** (28) PUMP INSTALLER **P. F. Beal & Sons, Inc.**

(29) TYPE **submersible** (30) MAKE **Goulds** (31) MODEL **5GS15412**

(32) MAXIMUM CAPACITY (GPM) **5 gpm** (33) PUMP INSTALLATION LEVEL FROM TOP OF CASING (Feet) **620'**

(34) METHOD OF DRILLING Rotary Cable Tool Other _____ (35) USE OF WATER (see instructions for choices) **residential**

(36) DATE DRILLING WORK STARTED **10/9/01** (37) DATE DRILLING WORK COMPLETED **10/11/01**

(38) DATE REPORT FILED **4/6/01** (39) DRILLER & COMPANY **Perry L. Beal P. F. Beal & Sons, Inc.** (40) DEC REGISTRATION NO. **NYRD10105**


665'
BOTTOM OF HOLE

* Show log of geologic materials encountered with depth below ground surface, water bearing beds and water levels in each; casings; screens; pump; additional pumping tests and other matters of interest, e.g., water quality (sulphur, salt, methane). Describe repair work. Attach separate sheet if necessary.

See further instructions titled "Instructions for New York State Well Completion Report".

OWNER COPY

SKETCH - Indicate north

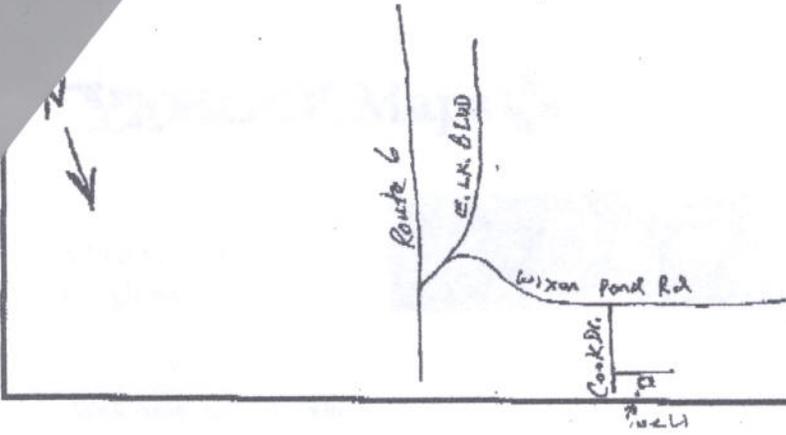

P1564



Yahoo! - Yellow Pages - Help

Powered by Mapquest.com (tm)

Y! DOMAINS:
Go global



Click for Details


Welcome, Guest User

Create My Locations - Sign In

Yahoo! Maps

★ cook

Save This Address

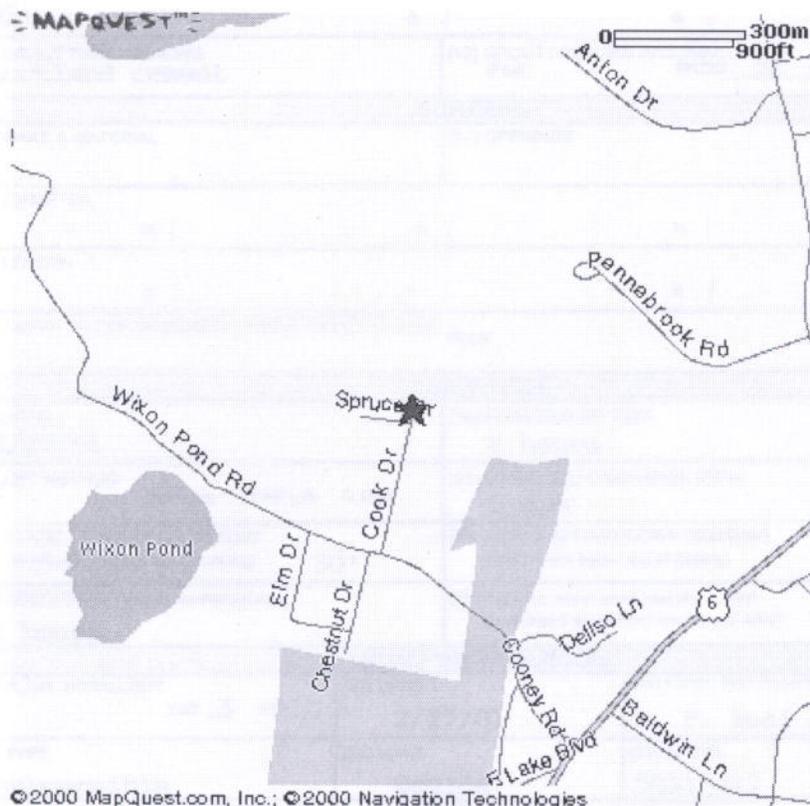

Zoom In

- [1]
- 2
- [3]
- [4]
- [5]
- [6]
- [7]
- [8]
- [9]
- [10]

Zoom Out

Printable Map

Email Map

Driving Directions

- To this location
- From this location

Map New Location

----- Sign In

Address, Intersection or Airport Code

City, State or Zip

United States

Get Map

Add Maps to My Yahoo!

Find Nearby Services

Nearby Businesses

- Car Rentals
- Gas Stations
- Hotels and Motels
- Restaurants

City Guide


- Yahoo! Traffic
- Yahoo! Travel
- Yahoo! Weather

Inside Yahoo!

- Yahoo! Classifieds
- Yahoo! Shopping
- Yahoo! Small

© 2000 MapQuest.com, Inc.; © 2000 Navigation Technologies

Business Locator - Click on business name to view the locations on map





1564

Target is 41° 23' 55"N, 73° 43' 38"W - LAKE CARMEL quad [\[Quad Info\]](#)

1:25,000 1:50,000 1:100,000 1:200,000

Small Medium Large

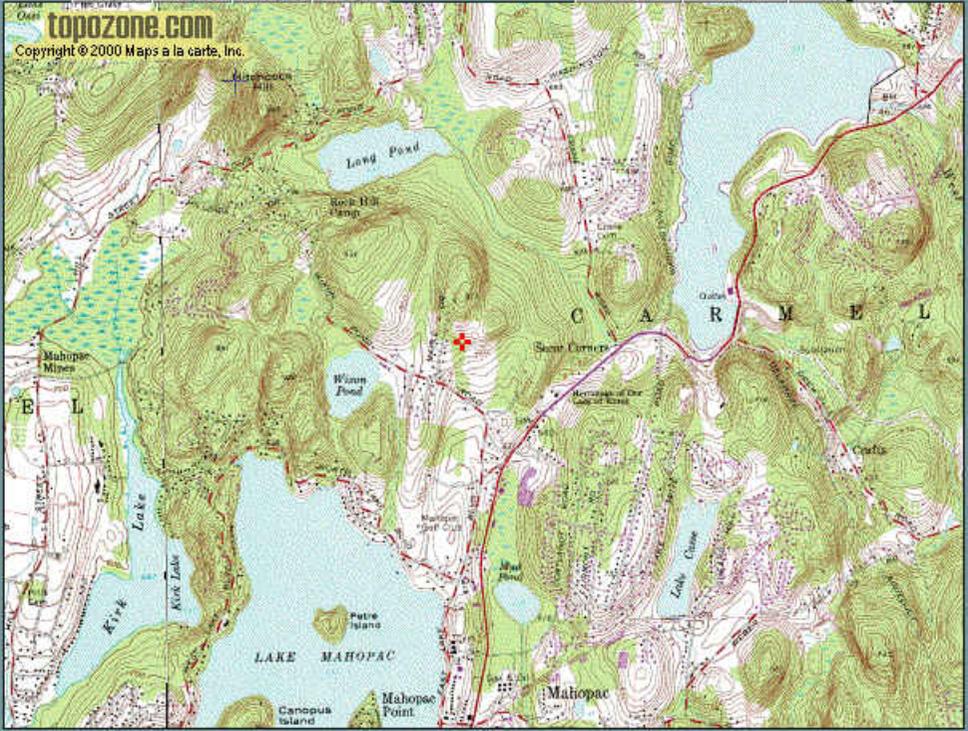

Coordinates (NAD27): UTM DD.DDDD D/M/S Show target symbol
