

C 179

41 25 34 73 44 27

WELL COMPLETION REPORT

3/71

C 179

LAKE CARMEL

PUTNAM COUNTY DEPARTMENT OF HEALTH

Division of Environmental Health Services
COUNTY OFFICE BUILDING - CARMEL, NEW YORK

This report is to be completed by well driller and submitted to County Health Department together with laboratory report of analysis of water sample indicating water is of satisfactory bacterial quality before certificate of construction compliance is issued.


REPORT MUST BE SUBMITTED WITHIN 30 DAYS OF WELL COMPLETION

P947

OWNER	NAME BELLSITE HOMES INC.		ADDRESS LAKE DRIVE, RFD #6, MAHOPAC, NEW YORK	
LOCATION OF WELL	LOGAN ROAD, MAHOPAC, NEW YORK		LOT 39	
PROPOSED USE OF WELL	<input checked="" type="checkbox"/> DOMESTIC	<input type="checkbox"/> BUSINESS ESTABLISHMENT	<input type="checkbox"/> FARM	<input type="checkbox"/> TEST WELL
	<input type="checkbox"/> PUBLIC SUPPLY	<input type="checkbox"/> INDUSTRIAL	<input type="checkbox"/> AIR CONDITIONING	<input type="checkbox"/> OTHER (Specify)
DRILLING EQUIPMENT	<input checked="" type="checkbox"/> ROTARY	<input type="checkbox"/> COMPRESSED AIR PERCUSSION	<input type="checkbox"/> CABLE PERCUSSION	<input type="checkbox"/> OTHER (Specify)
	LENGTH (feet)	DIAMETER (Inches)	WEIGHT PER FOOT	DRIVE SHOE
CASING DETAILS	10	six	19	<input checked="" type="checkbox"/> YES <input type="checkbox"/> NO
YIELD TEST	<input type="checkbox"/> BAILED	<input type="checkbox"/> PUMPED	<input checked="" type="checkbox"/> COMPRESSED AIR	HOURS
				five
WATER LEVEL	MEASURE FROM LAND SURFACE - STATIC (Specify feet)		DURING YIELD TEST (feet)	
	47 ft.		525 ft.	
SCREEN DETAILS	MAKE			LENGTH OPEN TO AQUIFER (feet)
	SLOT SIZE	DIAMETER (Inches)	IF GRAVEL PACKED:	Diameter of well including gravel pack (Inches):

850 L

DEPTH FROM LAND SURFACE FEET to FEET	FORMATION DESCRIPTION
0 to 2 1/2	Drilling in overburden - clay and earth Hit solid rock at 2 1/2 ft.
2 1/2 to 10	Drilling in rock - setting casing - grouted
10 to 525	Drilling in rock - granite

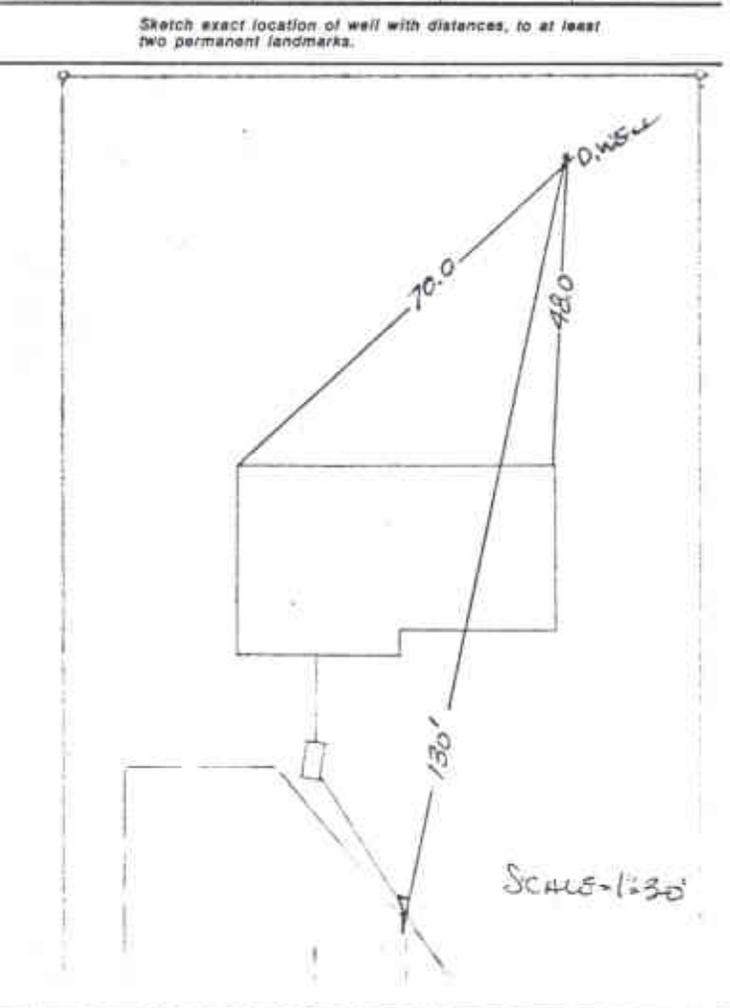

If yield was tested at different depths during drilling, list below

FEET	GALLONS PER MINUTE

DATE WELL COMPLETED 9/27/72	DATE OF REPORT 4/6/73	WELL DRILLER (Signature) P. F. BEAL & SONS, INC.
--------------------------------	--------------------------	---
