3

BREWSTER

PUTNAM COUNTY DEPARTMENT OF HEAL
Division of Environmental Health Services
COUNTY OFFICE BUILDING · CARMEL, NEW YO

This report is to be completed by well driller and submitted to County Health Department together with laboratory report of analysis of water sample indicating water is of satisfactory bacterial quality before certificate of construction compliance is issued.

REPORT MUST BE SUBMITTED WITHIN 30 DAYS OF WELL COMPLETION

41 22 56 73 36 20 1122

OWNER	NAME: Mr. John Mallon	ADDRESS: Lakeside Drive, Brewster, New York
LOCATION OF WELL	(No. & Street): Allview Avenue	(Town): Brewster, New York (Lot Number):
PROPOSED USE OF WELL	[X] DOMESTIC [ ] BUSINESS ESTABLISHMENT [ ] FARM [ ] TEST WELL [ ] PUBLIC SUPPLY [ ] INDUSTRIAL [ ] AIR CONDITIONING [ ] OTHER (Specify)	510 S
DRILLING EQUIPMENT	[ ] ROTARY [X] COMPRESSED AIR PERCUSSION [ ] CABLE PERCUSSION [ ] OTHER (Specify)	
CASING DETAILS	LENGTH (feet): 20'6" DIAMETER (inches): 6" WEIGHT PER FOOT: 17 [X] THREADED [ ] WELDED DRIVE SHOE [X] YES [ ] NO WAS CASING CUT OFF [X] YES [ ] NO	
YIELD TEST	[ ] BAILED [ ] PUMPED [X] COMPRESSED AIR HOURS: 4 G.P.M.: 20 YIELD (G.P.M.): 16	
WATER LEVEL	MEASURE FROM LAND SURFACE – STATIC (Specify feet): 20 DURING YIELD TEST (feet): 260 Depth of Completed Well (feet below land surface): 260	
SCREEN DETAILS	MAKE: SLOT SIZE: DIAMETER (inches): IF GRAVEL PACKED: Diameter of well including gravel pack (inches): GRAVEL SIZE (inches): LENGTH OPEN TO AQUIFER (feet): FROM (feet): TO (feet):	

DEPTH FROM LAND SURFACE FEET	to FEET	FORMATION DESCRIPTION
0	3	Top Soil
3	260	Medium-Hard Black & Grey Bedrock

Sketch exact location of well with distance to at least two permanent landmarks.

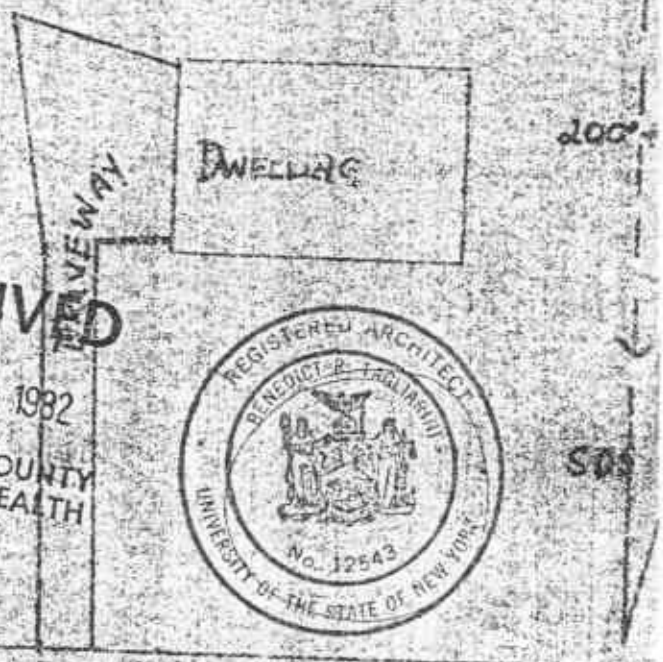

RECEIVED
DEC 13 1982
PUTNAM COUNTY
DEPT. OF HEALTH

REGISTERED ARCHITECT
BENEDICT R. TAGLIARINI
No. 12543
UNIVERSITY OF THE STATE OF NEW YORK

If yield was tested at different depths during drilling, list below

FEET	GALLONS PER MINUTE
170	2
194	2-3/4
233	3-1/2
245	12
260	16

DATE WELL COMPLETED	DATE OF REPORT	WELL DRILLER (Signature)
7/14/81	7/21/81	Robert H. Mill

Robert H. Mill, President-Mill Drilling, Inc.
