37 41 23 14 73 40 14 COUNTY OFFICE BUILDING - CARMEL, NEW YORK

This report is to be completed by well driller and submitted to County Health Department together with laboratory report of analysis of water sample indicating water is of satisfactory bacterial quality before certificate of construction compliance is issued.

REPORT MUST BE SUBMITTED WITHIN 30 DAYS OF WELL COMPLETION

P1155 LAKE CARMEL

OWNER	NAME: HOPTA, Andrew	ADDRESS: 43 Blackberry Drive, Brewster, NY 10509
LOCATION OF WELL	(No. & Street): Drewville Road,	(Town): Brewster, NY (Lot Number):

PROPOSED USE OF WELL: [X] DOMESTIC [ ] BUSINESS ESTABLISHMENT [ ] FARM [ ] TEST WELL [ ] PUBLIC SUPPLY [ ] INDUSTRIAL [ ] AIR CONDITIONING [ ] OTHER (Specify) 470, √

DRILLING EQUIPMENT: [ ] ROTARY [X] COMPRESSED AIR PERCUSSION [ ] CABLE PERCUSSION [ ] OTHER (Specify)

CASING DETAILS	LENGTH (feet)	DIAMETER (inches)	WEIGHT PER FOOT		DRIVE SHOE	WAS CASING GROUTED?
	24	6	19	[X] THREADED [ ] WELDED	[X] YES [ ] NO	[X] YES [ ] NO

YIELD TEST		HOURS	G.P.M.	YIELD (G.P.M.)
[ ] BAILED [X] PUMPED [ ] COMPRESSED AIR		49	20	25

WATER LEVEL	MEASURE FROM LAND SURFACE—STATIC (Specify feet)	DURING YIELD TEST (feet)	Depth of Completed Well in feet below land surface:
	52	205	840

SCREEN DETAILS	MAKE				LENGTH OPEN TO AQUIFER (feet)	
	SLOT SIZE	DIAMETER (inches)	IF GRAVEL PACKED:	Diameter of well including gravel pack (inches):	GRAVEL SIZE (inches)	FROM (feet) / TO (feet)

DEPTH FROM LAND SURFACE: FEET	to FEET	FORMATION DESCRIPTION
0	10	Silt, sand & gravel
10	75	Medium to hard granite
75	85	Soft seam, brown & green quartz
85	300	Medium to hard grey granite
300	410	Hard granite
410	500	Medium to hard fractured granite
500	640	Soft fractured granite
640	770	Medium to hard fractured granite
770	840	Soft fractured granite

If yield was tested at different depths during drilling, list below

FEET	GALLONS PER MINUTE

Sketch exact location of well with distances, to at least two permanent landmarks.

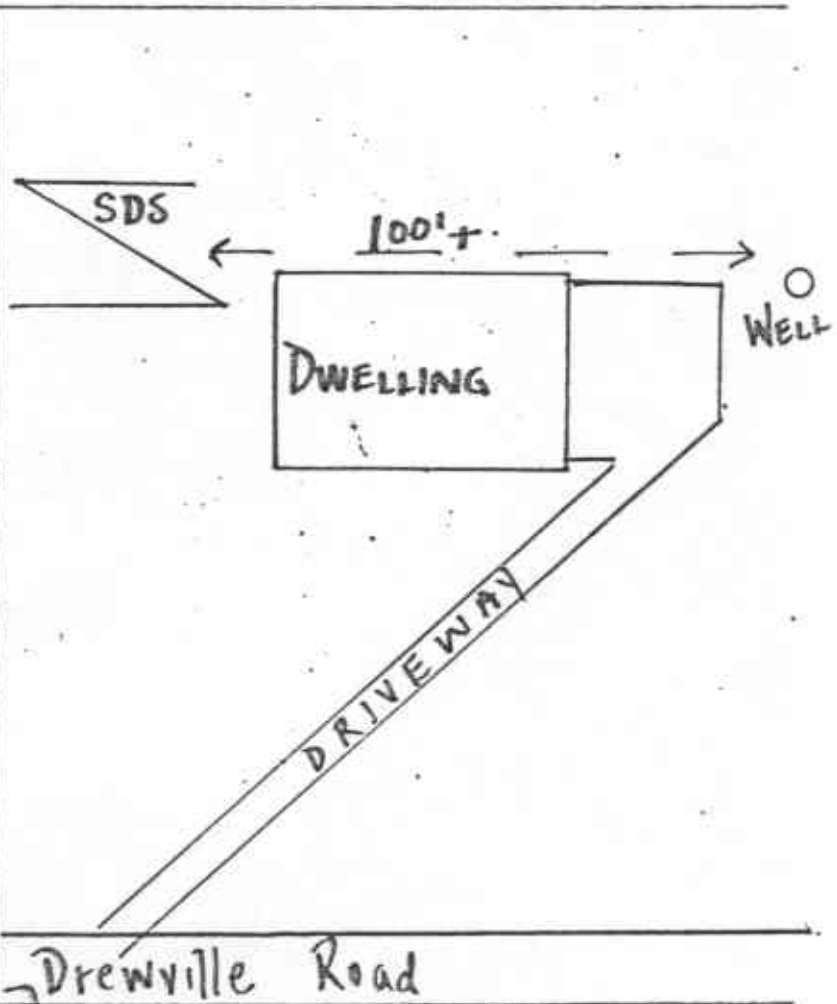

DATE WELL COMPLETED	DATE OF REPORT	WELL DRILLING CONTRACTOR (Signature)
4/10/84	6/13/84	Robert M. Mill, Pres.-MILL DRILLING, INC.
