WELL COMPLETION REPORT
2/71

C102 LAKE CARMEL 41 23 17 73 41 15

ERICH AABEL
PUTNAM COUNTY DEPARTMENT OF HEALTH
Division of Environmental Health Services
COUNTY OFFICE BUILDING - CARMEL, NEW YORK

This report is to be completed by well driller and submitted to County Health Department together with laboratory report of analysis of water sample indicating water is of satisfactory bacterial quality before certificate of construction compliance is issued.

REPORT MUST BE SUBMITTED WITHIN 30 DAYS OF WELL COMPLETION

P905

OWNER	NAME: ERICH AABEL (No. & Street)		ADDRESS: DREWVILLE ROAD, BARMEL, NEW YORK (Town) (Lot Number)			
LOCATION OF WELL	DREWVILLE ROAD, CARMEL, NEW YORK					
PROPOSED USE OF WELL	[X] DOMESTIC	[ ] BUSINESS ESTABLISHMENT	[ ] FARM	[ ] TEST WELL		
	[ ] PUBLIC SUPPLY	[ ] INDUSTRIAL	[ ] AIR CONDITIONING	[ ] OTHER (Specify) 365 C		
DRILLING EQUIPMENT	[X] ROTARY	[ ] COMPRESSED AIR PERCUSSION	[ ] CABLE PERCUSSION	[ ] OTHER (Specify)		
CASING DETAILS	LENGTH (feet): 20	DIAMETER (inches): six	WEIGHT PER FOOT: 19	[X] THREADED [ ] WELDED	DRIVE SHOE [X] YES [ ] NO	WAS CASING GROUTED? [X] YES [ ] NO
YIELD TEST	[ ] BAILED	[ ] PUMPED	[X] COMPRESSED AIR	HOURS: 5	G.P.M.: 5	YIELD (G.P.M.): 5 GPM
WATER LEVEL	MEASURE FROM LAND SURFACE—STATIC (Specify feet): 31 ft.	DURING YIELD TEST (feet):		Depth of Completed Well in feet below land surface: 175 ft.		
SCREEN DETAILS	MAKE					LENGTH OPEN TO AQUIFER (feet)
	SLOT SIZE	DIAMETER (inches)	IF GRAVEL PACKED:	Diameter of well including gravel pack (inches):	GRAVEL SIZE (inches)	FROM (feet) / TO (feet)

DEPTH FROM LAND SURFACE FEET	to FEET	FORMATION DESCRIPTION
0	5	Drilling in overburden-earth
		Hit solid rock at 5 ft.
5	20	Drilling in solid rock - setting casing - grouted
20	175	Drilling in rock - granite

If yield was tested at different depths during drilling, list below

FEET	GALLONS PER MINUTE

Sketch exact location of well with distances, to at least two permanent landmarks.

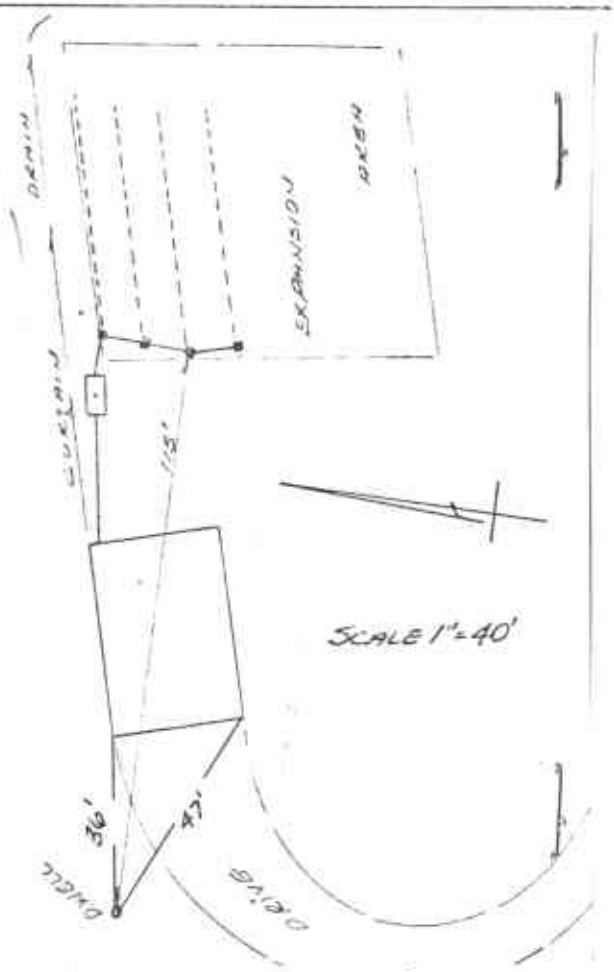

DATE WELL COMPLETED	DATE OF BILLING	WELL DRILLER (Signature)
9/9/71	6/26/73	P. F. BEAL & SONS, INC. Malcolm H. Beal Pres
